



ବିଜ୍ଞାପିତ ଅଂଳେ ପରିଷଦ, ରେଡାଖୋଲ

OFFICE OF THE
NOTIFIED AREA COUNCIL, REDHAKHOL.
(ODISHA), DIST- SAMBALPUR



E-mail:- eonacrdl@gmail.com, Ph.No/ Fax No. 06644- 253466

No. 1382 /NAC Dated. 20 .07.2024


QUOTATION CALL NOTICE

Sealed quotations are invited from the interested parties/suppliers having GSTIN for supply and install of four seated prefab Toilet with Tensile Fabric & MS canopy with all types of civil work at different places of Redhakhol NAC. The quotations should reach the undersigned on or before 02.00 P.M of dtd 29.07.2024 through Regd. Post/Speed Post/Courier which shall be opened on the same day at 4.00 P.M in the presence of the quotationers / their representatives/ authorized agent. Technical evaluation will be based as per mentioned additional terms and condition failing which the bidder may be disqualified. The rate shall be quoted including transportation, labour and installation charges of Toilets and other taxes may be quoted as applicable for the prescribed specification. The bidder should submit the Technical and Financial bid in separate envelope mentioning each. The quotation shall accompany with paper cost of Rs 4,000/- in shape of Demand Draft/ Ban Draft in the name of Executive Officer, NAC, Redhakhol payable at Rairakhhol. The successful quotationers should complete the work within 30 days for one unit from the issue of the order, failing which the order shall stand cancelled. No extra charges will be demand after issue of the work order and stands valid till completion of the project.


The undersigned shall reserve the right to reject any or all quotation without assigning any reason thereof.


Executive Officer,
NAC, Redhakhol.

Memo No. 1383 Date. 20.07.2024
Copy to the office notice board / Sub-Collector, Rairakhhol/
B.D.O Rairakhhol for information with a request to display in their notice board.



Executive Officer,
NAC, Redhakhol

Memo No. 1384 Date. 20 .07.2024
Copy to DIO, NIC, Sambalpur/ NAC website for wide
publication of the notice


Executive Officer,
NAC, Redhakhol

TECHNICAL SPECIFICATION FOR 04 SEATED PREFAB TOILET WITH TENSILE FABRIC AND MS CONOPY INCLUDING ALL TYPE OF CIVIL WORK (CIVIL FOUNDATION, WASTE MANAGEMENT FACILITY):

TOILET SPECIFICATION	
Product Description	04 seated prefab toilet with tensile fabric and MS Canopy including all type of civil work (civil foundation & waste management facility)
Quantity Required	
Foundation	Brick Foundation as per Standard Specs with a depth of 300 mm below ground level and 300 mm above ground level for anchor/column Locations: 9" thick Brick work for foundation work
Toilet size	The structure size should be 1220 mm x 915 mm, Toilet structure height (except the foundation structure)-2025 mm (i.e Bottom to Top roof)
Toilet tub	EWC Pan 04 nos EWC pan Size 520 x 360 x 390 (Cera/ Sanitation/Johnson/ Equivalent) with Antiskid Tiles of 12" x 12" (Somani /Cera / Johnson/ Nitco/ Equivalent)
Paneling	<ul style="list-style-type: none"> Each wall consists of 4 sandwich panels (Inc. of top louver panel on each side). Sandwich panel size 995 mm x 650 mm & 695 mm x 695 mm All 4 top wall panels to have single-skin louver panels (150 mm) of 0.6 mm Galvanized Plain powder-coated sheet Each wall panel is to be 40 mm thick Sandwich Panels made of 0.6 mm thick, Min 240 MPa Yield Strength (YS), Min 340 Ultimate Tensile Strength (UTS) zero spangled skin passed Tension leveled, Restriction of Hazardous Substance (ROHS) compliant, 120 GSM galvanized plain, powder coated cold rolled sheet with insulation (38 mm EPS (Expanded Polystyrene) of density 16 kg/m3) inside it. The bottommost panel on 3 sides in each compartment is to have SS 304 in the interiors upto 125 mm from the floor that is to be riveted over powder coated galvanized plain sheet.
Doors	Door size 1790 mm x 649 mm x 40 mm thickness (made of 0.6 mm Galvanized plain powder coated steel) inclusive of standard accessories i.e 2 nos of the handle (6 inches), 1 L drop with plastic bush 1 No of Tower bolt (6 inch) hinges and screws.
SIDE PLATFORM	
Type	Brickwork platform (4' x 3')
Material	Bricks, parking tiles, Cement, Sand
Ladder	Brickwork steps with parking tiles
SLUDGE TANK	
Capacity	1700 Ltr (4' x 4' x 4' soak pit) or RCC ring with 3' diameter 4 Qty with RCC cover
Material	Brick, cement, sand, aggregate
Fittings	SWR PVC 110 mm pipe for toilet and soak pit connection
Canopy	MS partition 0.4 mm thick PPGI Roof sheet & 30 x 30 mm MS square tube with 0.5 MM MS sheet for partition
Tensile canopy	4' x 3' Tensile fabric canopy above wash basin 12 sqft- 02 nos
Water tank and frame	200 litres on each cabin with required UPVC plumbing fitments along with tank frame Tank Brand: Plasto/ Sintex/ Paras/ equivalent
Electric fittings	1 CFL t5 Wt (Wipro/Syska or similar)n & 1 Modular switch (Anchor/Amron) in each compartment and required internal wiring, wire (Polycab/ CRV/ Equivalent) 1.5 square mm
Plumbing material	All internal piping with UPVC pipe of nominal dia 20 mm with necessary unions for maintenance purposes & stop cocks. Paras /Astral or similar: one bib-cock tap in each compartment. One stop-cock each for controlling water flow.


 07-2024
Junior Engineer
N.A.C. Redhakhol


Executive Officer
Notified Area Council
Redhakhol

Financial Bid

To

The Executive Officer
NAC, Redhakhol

Sub:- Supply of Four seated Prefab Toilet with Tensile Fabric & MS
conopy with all type of civil work as per Specification.

Ref:- Quotation Call Notice No. _____ Dated _____

Sir,

I/We _____ persons/firms/ suppliers/
agency are willing to offer out price based on standard design, standard material
specification and standard term and condition of supply

Sl. No	Product Description	Per unit (04 seated)	Amount including Transportation and all taxes

Yours faithfully

(Signature with seal and stamp)


20/07/2024.
Junior Engineer
N.A.C. Redhakhol



20/07/2024/
Executive Officer
Notified Area Council
Redhakhol

ADDITIONAL TERMS & CONDITION (TECHNICAL EVALUATION)

1. Bidder should submit PAN, GST, Udyam MSME Certificate. Incorporation/Shop Act/ Registration Certificate.
2. Goods should be delivered on site delivery basis with unloading & complete installation.
3. Bidder should not be under liquidation, court proceedings, should not be bankrupt. Bidder to submit undertaking to his effect with bid.
4. Bidder should submit valid OEM certificate with OEM turnover.
5. Bidder should submit last 3 years ITR copy ending with 23-24 and turnover certificate on CA letter head.
6. Bidder should submit Prefab work order from Government department.
7. Bidder should submit tensile fabric work order in Odisha State Government in financial year 2022-23 to 2023-24 with completion certificate and Geotag Image.
8. Bidder should submit Prefab Toilet work order from Odisha State.
9. Bidder's offer is liable to be rejected if they donot submit any of the certificate/documents in the bid documents.
10. The undersigned shall reserve the right to reject any or all quotation without assigning any reason thereof.


20/07/2024
Executive Officer
NAC, Redhakhhol


LAYOUT FOR PREFAB TOILET:

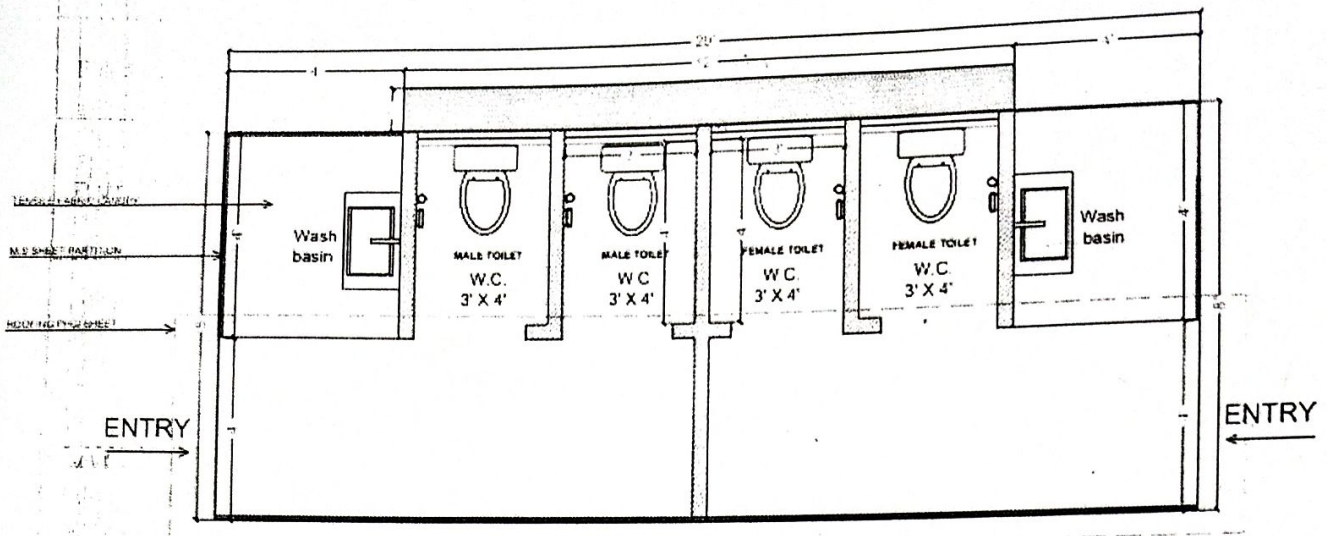

TOILET FLOOR PLAN

TOTAL AREA - 191 SQ FT

FRONT ELEVATION FOR PREFAB TOILET:

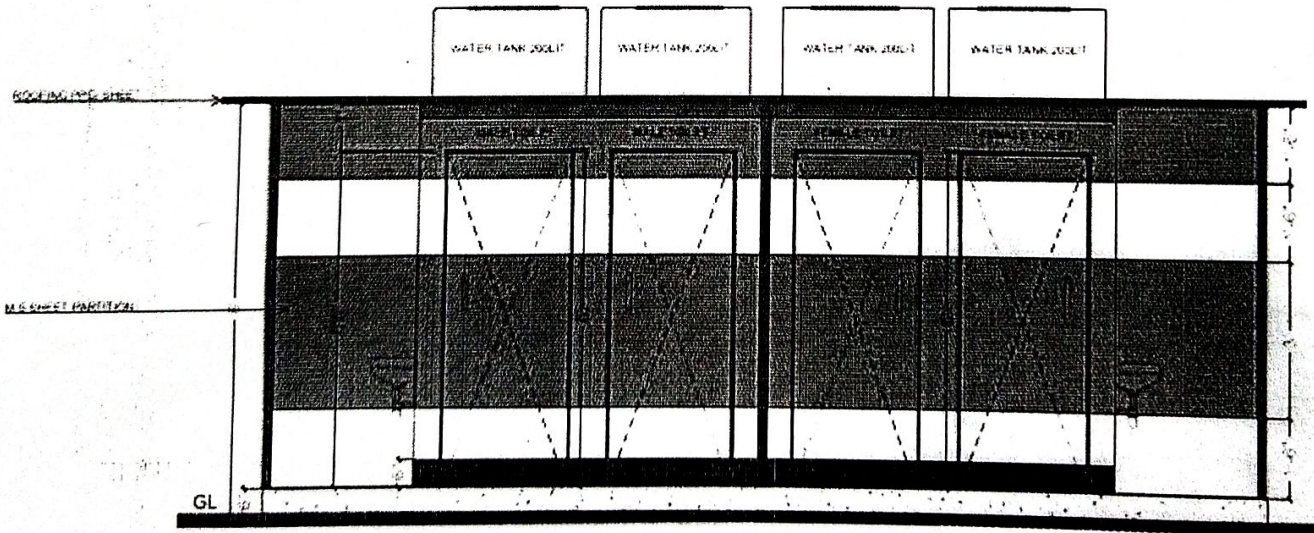

FRONT ELEVATION

[Signature]
20.07.2024
Junior Engineer
N.A.C. Redhakhol

[Signature]
20/07/2024
Executive Officer
Notified Area Council
Redhakhol
